




NGAN FIBER DEEP PROJECT SACRAMENTO AREA

■ COMPLETED

SCHEDULE

| AREA | | COMPLETE DATE |
|------|----|----------------|
| QACX | 32 | 1902 3/28/2018 |
| QAD6 | 25 | 1393 4/12/2018 |
| QADF | 15 | 1441 4/30/2018 |
| QABC | 19 | 1158 5/2/2018 |
| QABK | 5 | 292 5/7/2018 |
| QACT | 13 | 826 5/8/2018 |
| QACN | 19 | 1251 5/9/2018 |
| QADD | 18 | 1482 5/14/2018 |
| QADZ | 20 | 1498 5/17/2018 |
| QAAS | 13 | 694 5/22/2018 |
| QACJ | 45 | 2286 5/24/2018 |
| QACP | 11 | 574 6/4/2018 |
| QACK | 8 | 543 6/6/2018 |
| QAEC | 14 | 825 6/7/2018 |
| QAEA | 20 | 1238 6/14/2018 |
| QACD | 28 | 1471 6/19/2018 |
| QADA | 20 | 1489 |
| QADP | 24 | 1384 |
| QACM | 13 | 916 |

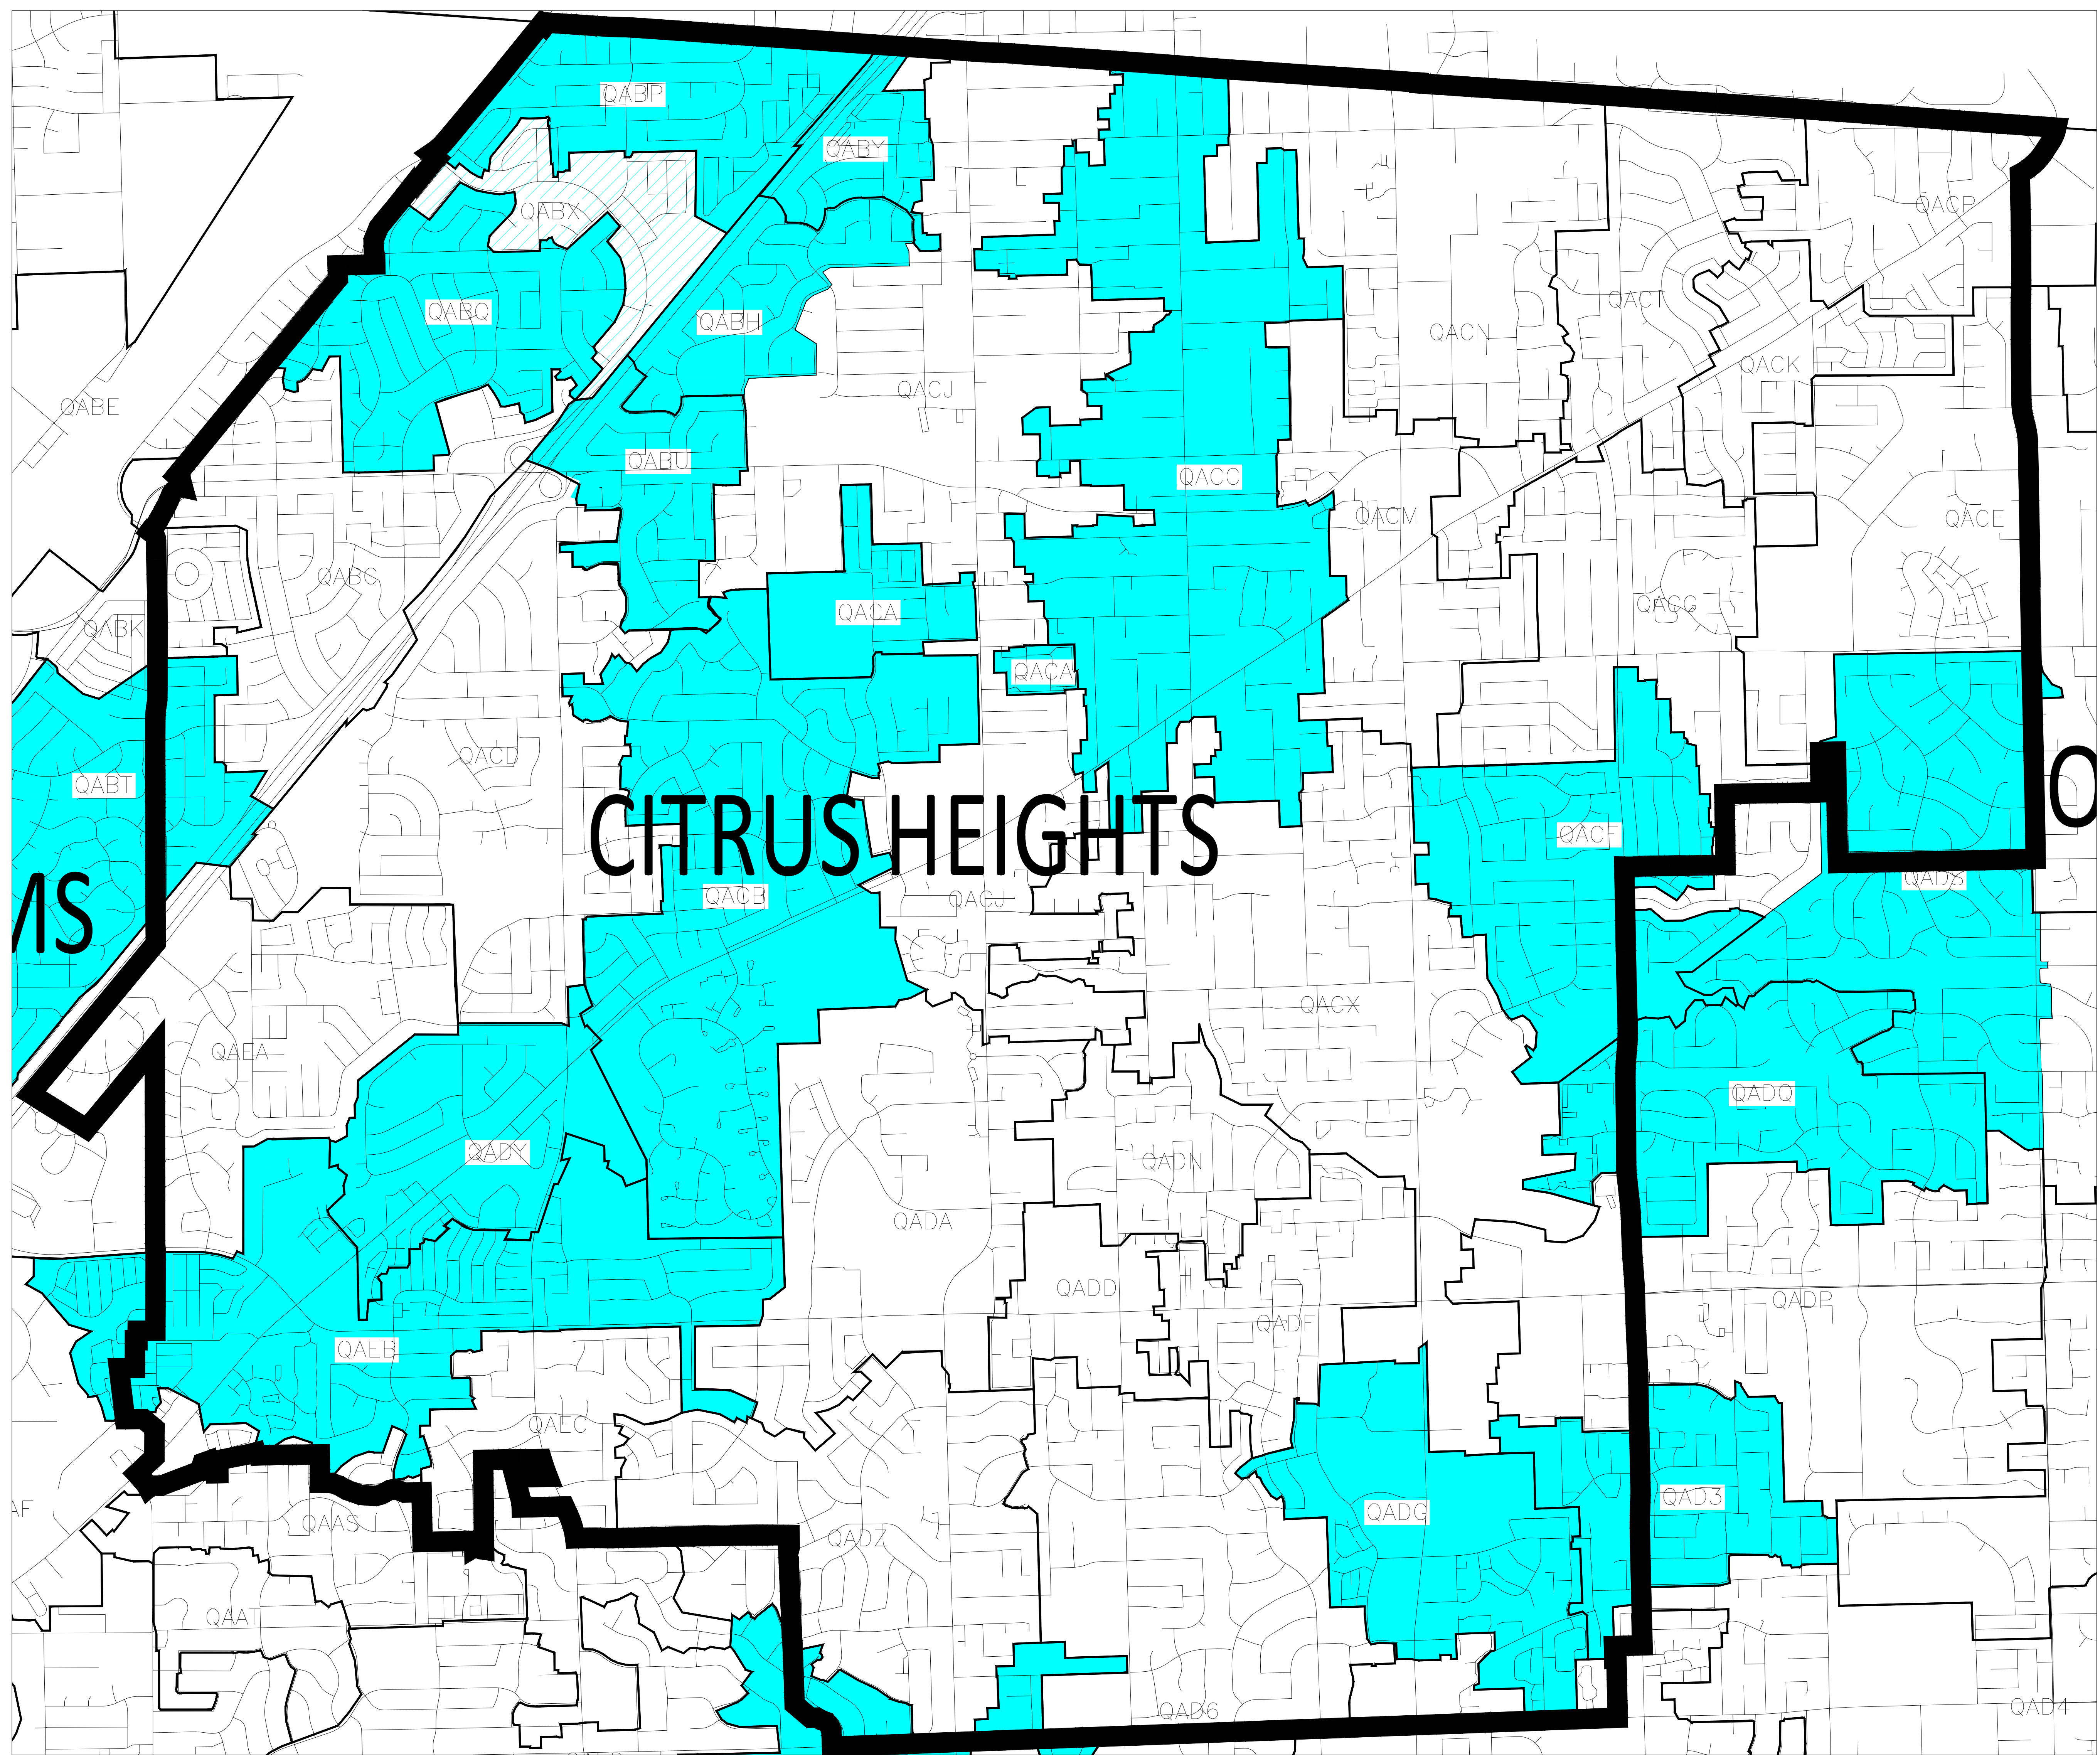

NOTE: ALL DATA SUBJECT TO CHANGE
